1st and final Bill

KSR dt. 465/26/10/16

M. A. R. 57 (Rule 116)

Measurement Book

No. B 489101

Improvements of ce roads & Rce drains at 8th, 9th cross and other roads near pipe line in ward No. 13, Shettyhalli Sub Division,

Serial No. ...

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency ..... Technical Manager (Level 5) KRIDL

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Job code:- 013-17-000009				Est. cost : 50.00 lakhs		
	A.S. No:- AC/DZ/AS/28/2016-17. Dt. 30.08.2016						
	T.S. No:- CE/DZ/TS/41/2016-17. Dt. 01.09.2016						
	W.O. No:- BBMP/EE/DD/W0/62/2016-17. Dt 02.09.2016.						
	Date of recording:- 19-9-16						
①	Earthworks excavation by manual means in ordinary soil involving in average horizontal throw upto to 2m & an average lift upto 1.5m. excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications						
	As per Premeasurement Qty recorded in the MB Page No. 48916 to 62 vide item No. ①.		i.e			484.29 Cum	
			@ Rate of	83.16/Cum		= ₹ 40,274/-	

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	⑥ Providing and removing centering, shuttering, stopping etc., and removal of form works for vertical surface such as walls of any thickness, including attached pilasters, buttresses, plinth and string courses cost of all materials, labour complete as per specifications. as per premeasurement Sh recorded in the MB page No. 489166 vide item no ⑥ i.e @ rate ₹ 301.04/sqm					2322.60 Sqm = ₹ 6,99,196/- 712388 -	
	⑦ Providing and laying reinforced cement precast slabs of mix CC 1:1½:3 using 20mm ϕ down size graded granite metal using HYSD 10mm dia steel @ 10 nos/cc bothways & complete as per specifications.						
	8th cross	18	0.60	0.90		9.72	
	9th cross	18	0.60	0.90		9.72	
	Sandi drain	8	0.60	0.96		4.32	

Serial No. .....
Name of Work .....
Name of Contractor of
Date of commenceme

Date	Full descrip
1	
	1st cro 2nd cro 11th cross missed ϕ16 pipeline 10th cross

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(8) Disposal of debris to the final place of disposal with all lead and lift and as direction by the engineer in charge of the works., lead 10Km.						
	Sch wide item No. (1) -					484.29 Cum	
						@ rate of ₹ 81.73/Cum =	₹ 39,581/-
		4536786 =				Sub Total =	₹ 45,23,590/-
		362942 =				KR DL charges 8% =	₹ 3,61,887/-
		4899728 =				QC 1% =	₹ 50,000/-
						Total =	₹ 49,35,477/-

Chd & Re

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Certificate:
(1) The works done by contractor satisfactorily
(2) The contractor has removed all debris from works spot
(3) There is no departmental issues.

19-4-18

Serial No. .....
Name of Work .....
Name of Contractor of
Date of commencemer

Date | Full descrip
1 | 2

4899728=
4259298=

M. A. R. 57 (Rule 116)
Measurement Book

No. B 489105

Serial No. .....
Name of Work ..... 640430=00 From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8

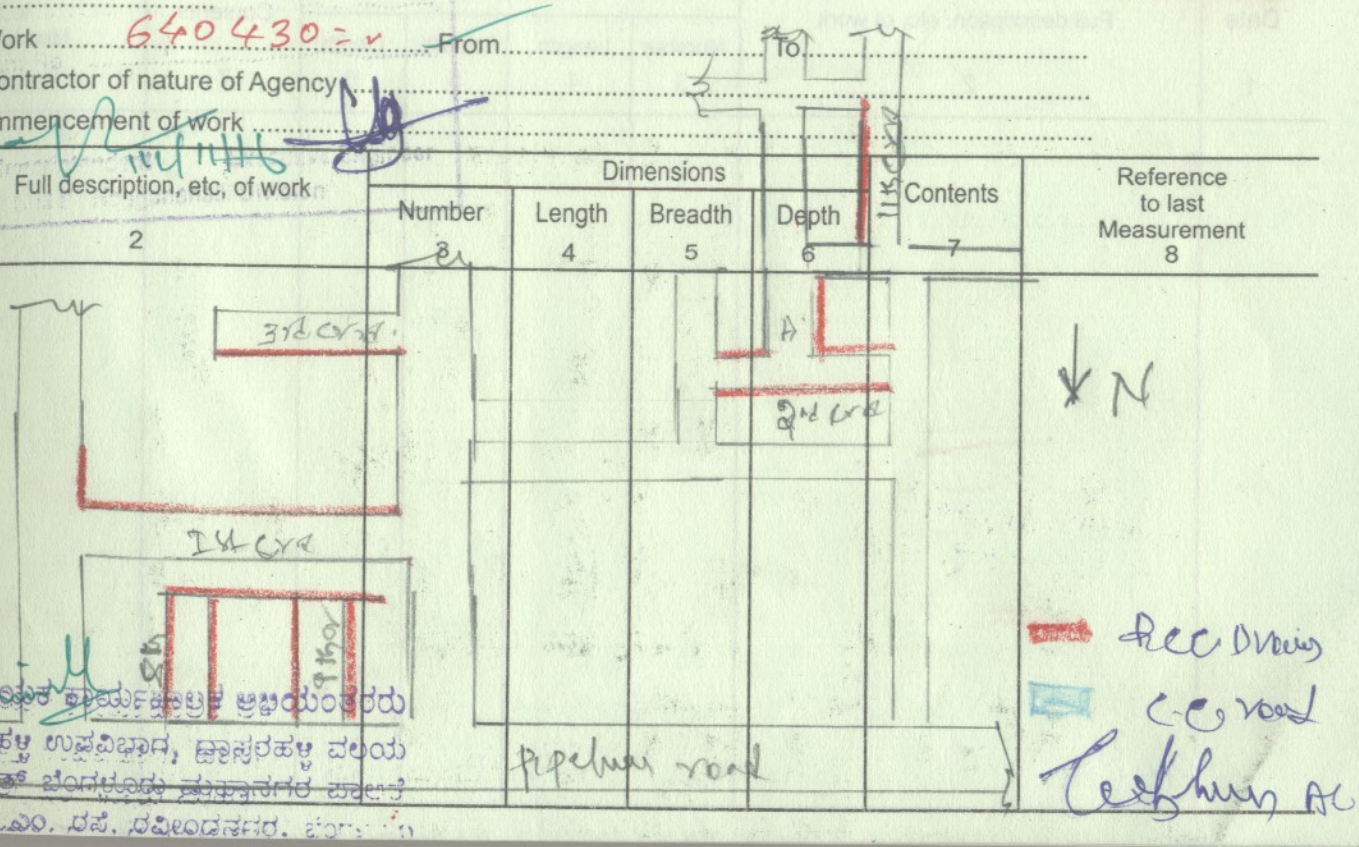

ಪತ್ರಾಂಶದ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಡಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಪಾಲಿಕೆಗಳ ಪಾಲಿಕೆ
ಬಿಬಿಎಂಪಿ, ದಪೆ, ದಾಸರಹಳ್ಳಿ.

Checked AE

4899728=
4259298=

M. A. R. 57 (Rule 116)
Measurement Book

No. B 489105

Serial No. .....
Name of Work ..... 640430=00 From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8

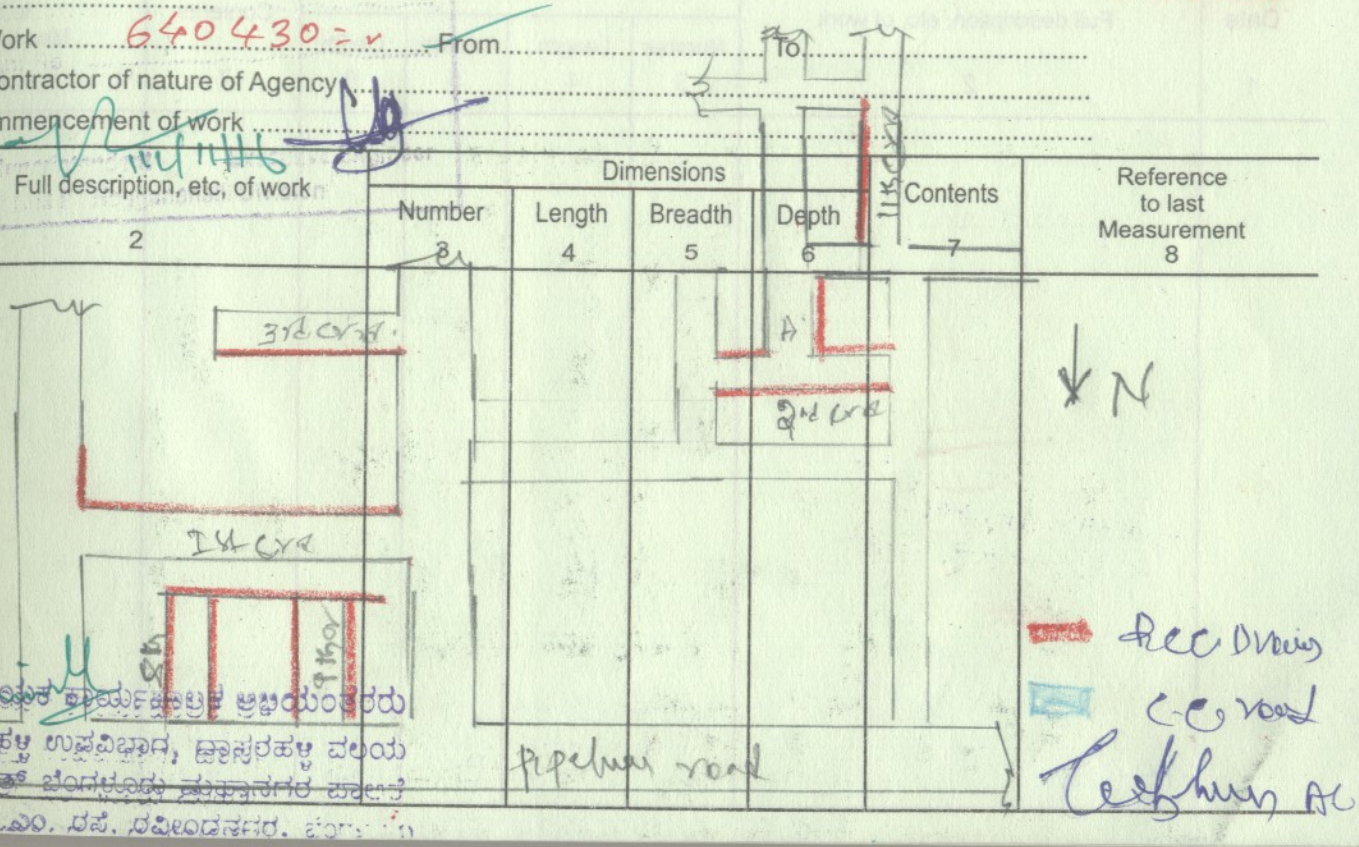

ಪತ್ರಾಂಶದ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಡಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಪಾಲಿಕೆಗಳ ಪಾಲಿಕೆ
ಬಿಬಿಎಂಪಿ, ದಪೆ, ದಾಸರಹಳ್ಳಿ.

Checked AE
